

Executive Summary


Brookings County Detention Center Expansion and Remodel

What's New

We are excited to get this project started and are happy to be a part of it. We look forward to the months to come and the progress that will be made.

In the beginning there are a lot of things that are happening behind the scenes with material shop drawings, color selections, etc. This allows us to review and get material ordered, so we have them on site when needed for installation.

On site, we have completed the site demolition and clearing. We now have site utilities being reviewed and installed. The next steps will be building footings and foundations. We are also working with the Sheriff's Department for temporary means related to their 24/7 operation.

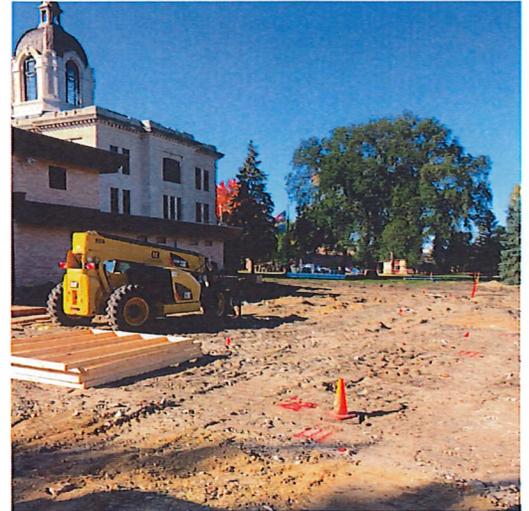

The Past Month (September)

1. Site clearing and demolition
2. Start of site utilities installation
3. Temporary constructions for the Sheriff's Department

Coming Up in the Next Month (October)

1. Continue with site utilities
2. Temporary perimeter site fencing
3. Footings and foundations
4. Earthwork (building pad)

Schedule Update

1. Original construction completion date: 6/13/22
2. Current updated construction completion date: 6/13/22

Budget Update

1. Original GMP/Contract: \$15,193,634
2. Updated GMP (Thru CO): \$15,193,634

